

# ECompendium

for Completed works

Home List of Projects Report Report Excel

Hello Law! Change Password Logout

Find Project:

Search


Back

Sort




### Repair and renovation of Directorate of Litigation, Jammu building by way of civil works at High court, Jammu.

Sector	UT
Date of Commencement	24/05/2023
Date of Completion	31/10/2023
AA Cost in lacs	18.02
Completion Cost in lacs	14.49
No. of Beneficiaries/ Souls Benefited	All employees of the Directorate of Litigation Jammu

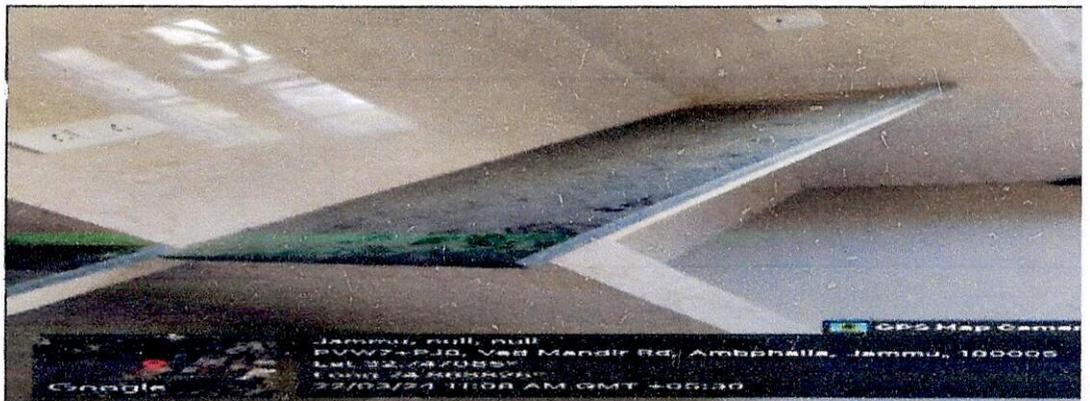

### Renovation of Judiical Quaters 03 Nos at ,Amphala Jammu

Sector	UT
Date of Commencement	21/06/2021
Date of Completion	31/08/2023
AA Cost in lacs	16.45
Completion Cost in lacs	9.82

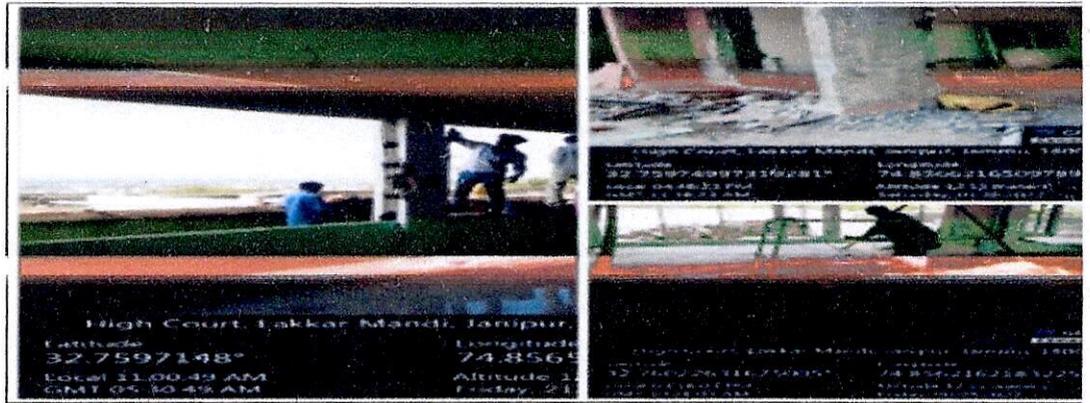

**Renovation of Pantry, toilet, tiling of terrace and office Chambers of Hon'ble Chief Justice at High Court, Jammu**

Sector	UT
Date of Commencement	29/06/2022
Date of Completion	31/07/2023
AA Cost in lacs	35.97
Completion Cost in lacs	28.3
No. of Beneficiaries/ Souls Benefited	Chief Justice Office



**Repair/renovation of newly created Court (Fastrack Court) Jammu**


Sector	UT
Date of Commencement	20/09/2022
Date of Completion	31/08/2023
AA Cost in lacs	16.94
Completion Cost in lacs	15
No. of Beneficiaries/ Souls Benefited	All Litigants of Jammu Division



**Construction of Room for accommodation of record at**

### District Court Jammu

<b>Sector</b>	UT
<b>Date of Commencement</b>	27/09/2022
<b>Date of Completion</b>	30/04/2023
<b>AA Cost in lacs</b>	3.12
<b>Completion Cost in lacs</b>	2.97
<b>No. of Beneficiaries/ Souls Benefited</b>	Employees of District Court Jammu

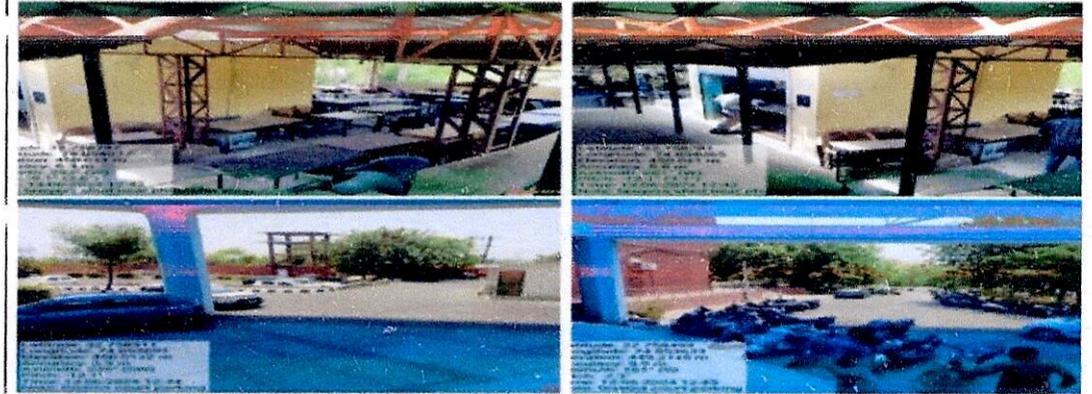


### Upgradation of Various works at High Court & District Court Complex Jammu

<b>Sector</b>	UT
<b>Date of Commencement</b>	23/05/2023
<b>Date of Completion</b>	31/10/2023
<b>AA Cost in lacs</b>	24.45
<b>Completion Cost in lacs</b>	20.94
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of District Court Jammu




### Utilization of available premises of Canteen at ground floor of District Court Jammu for accommodation of POCSO Court and its staff at District Court Complex Janipur Jammu

<b>Sector</b>	UT
<b>Date of Commencement</b>	24/05/2023
<b>Date of Completion</b>	29/02/2024
<b>AA Cost in lacs</b>	26.78
<b>Completion Cost in lacs</b>	18.71
<b>No. of Beneficiaries/ Souls Benefited</b>	All litigants regarding POCSO cases

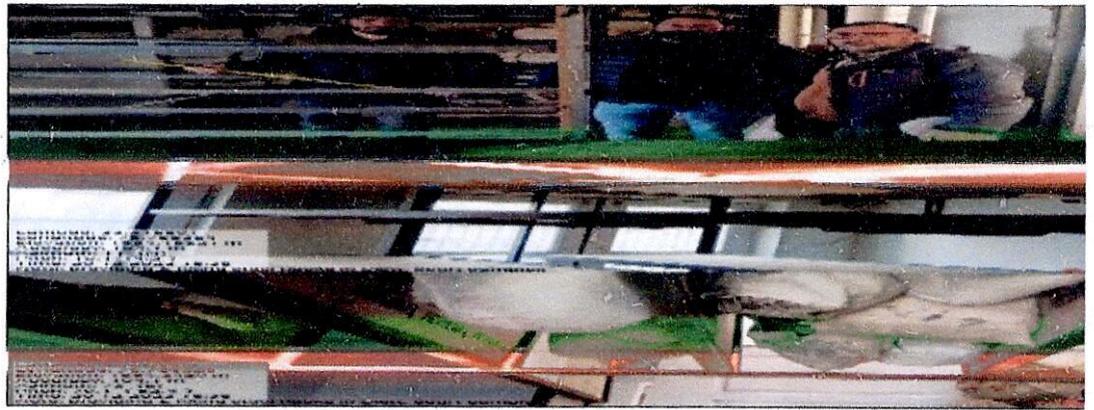


**Construction of racks for maintenance of Record at District & Session Court Kishtwar**

<b>Sector</b>	UT
<b>Date of Commencement</b>	23/07/2022
<b>Date of Completion</b>	31/03/2023
<b>AA Cost in lacs</b>	1.98
<b>Completion Cost in lacs</b>	1.86
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of District and Session Court Kishtwar

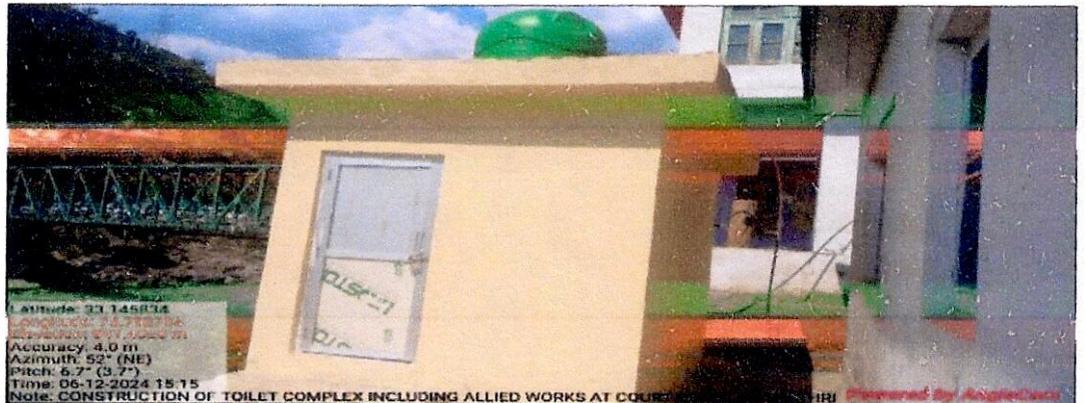

**Toilet block and allied works at Court Complex Thathri**

<b>Sector</b>	UT
<b>Date of Commencement</b>	07/07/2022
<b>Date of Completion</b>	30/06/2023
<b>AA Cost in lacs</b>	4.2
<b>Completion Cost in lacs</b>	2.02
<b>No. of Beneficiaries/ Souls Benefited</b>	All empoyess of the Thatri Court

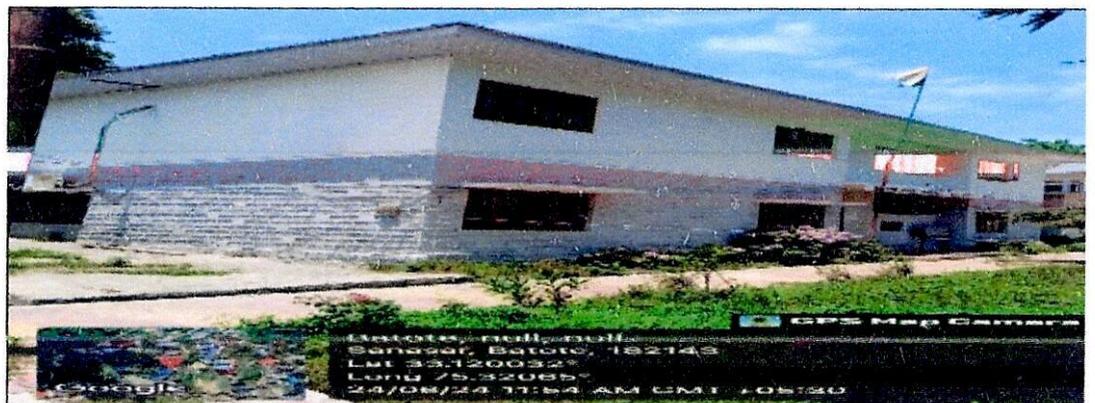

**Repair/renovation of building & boundary wall of Court Complex at Batote.**

<b>Sector</b>	UT
<b>Date of Commencement</b>	30/04/2023

<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	66.65
<b>Completion Cost in lacs</b>	66.65
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of Court Batote

1 2

Total Records : 17

© 2022 - ECompendium

# ECompendium

for Completed works

Home List of Projects Report Report Excel

Hello Law! Change Password Logout

Find Project:

Search

Back

Sort



**Repair/maintenance of Audio-video system installed in the Auditorium of J&K Judaical Academy and repairing of Podium, heating system and other allied works at Srinagar**

<b>Sector</b>	UT
<b>Date of Commencement</b>	09/05/2022
<b>Date of Completion</b>	24/05/2024
<b>AA Cost in lacs</b>	22.48
<b>Completion Cost in lacs</b>	22.22
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of Judicial Academy



**Construction of Common Washroom Block / Public Toilet Blocks (Male / Female) and Reverse Osmosis (ROs) at Munsiff Court Gandoh**


<b>Sector</b>	UT
<b>Date of Commencement</b>	23/05/2023

<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	3.45
<b>Completion Cost in lacs</b>	3.35
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of Gandoh Court



**Supply, Installation of CCTV Surveillance at District Court at Mominabad, Srinagar ( Phase -I)**


<b>Sector</b>	UT
<b>Date of Commencement</b>	17/10/2019
<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	72.34
<b>Completion Cost in lacs</b>	32.24
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees and litigants of District Court Moominabad

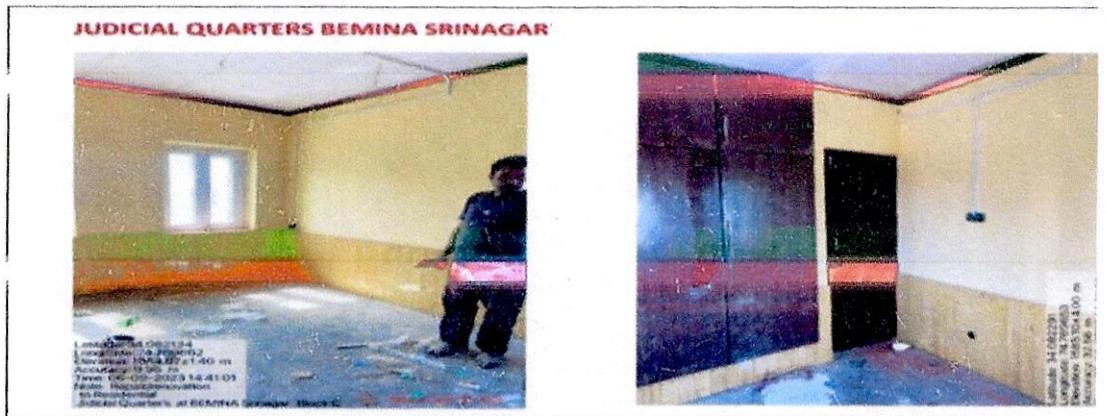

**Renovation/repairs to residential Judicial Quarters at Bemina Srinagar**


<b>Sector</b>	UT
<b>Date of Commencement</b>	23/05/2023
<b>Date of Completion</b>	29/02/2024
<b>AA Cost in lacs</b>	51.14
<b>Completion Cost in lacs</b>	41.47
<b>No. of Beneficiaries/ Souls Benefited</b>	Judicial Officers

**AUDITORIUM GALLERY HIGH COURT SRINAGAR**

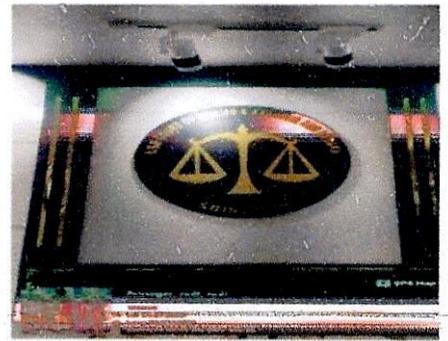


**Upgradation/Renovation of auditorium (Gallery) at High Court Srinagar**

<b>Sector</b>	UT
<b>Date of Commencement</b>	13/03/2023
<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	11.31
<b>Completion Cost in lacs</b>	10.56
<b>No. of Beneficiaries/ Souls Benefited</b>	All employees of High Court Srinagar

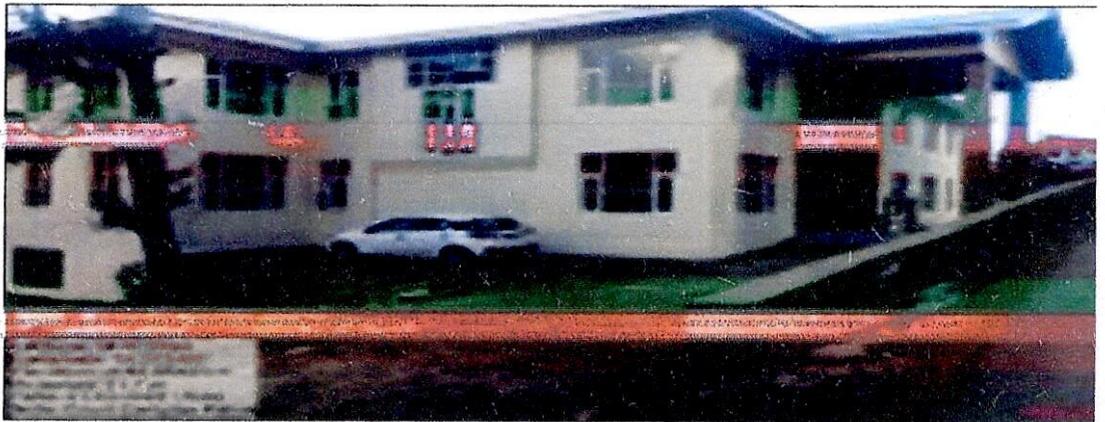

**Construction of Munsiff Court (Addl Mobile Magistrate) at Pahalgam**

<b>Sector</b>	UT
<b>Date of Commencement</b>	07/01/2020
<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	614.00
<b>Completion Cost in lacs</b>	460.00
<b>No. of Beneficiaries/ Souls Benefited</b>	All population of Pahalgam area

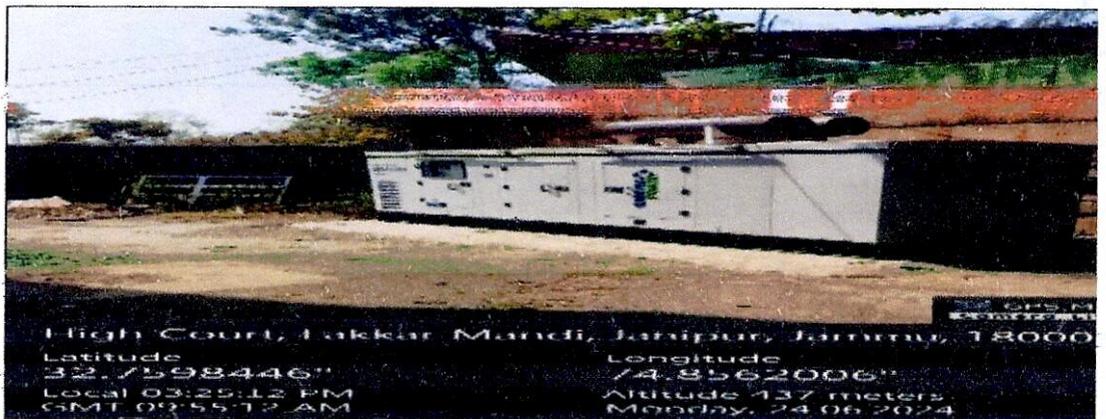

**Providing of 500 KV standby transformer at High Court Jammu**

<b>Sector</b>	UT
<b>Date of Commencement</b>	22/11/2022
<b>Date of Completion</b>	31/03/2024
<b>AA Cost in lacs</b>	47.80
<i>Completion Cost in lacs</i>	43.50
<b>No. of Beneficiaries/ Souls Benefited</b>	All the employees High Court of Jammu

1 2

Total Records : 17

© 2022 - ECompendium
